





Acceptance of Work: Northeast Interceptor Joint Grouting MH10-112 to MH10-106




Project Location and Scope

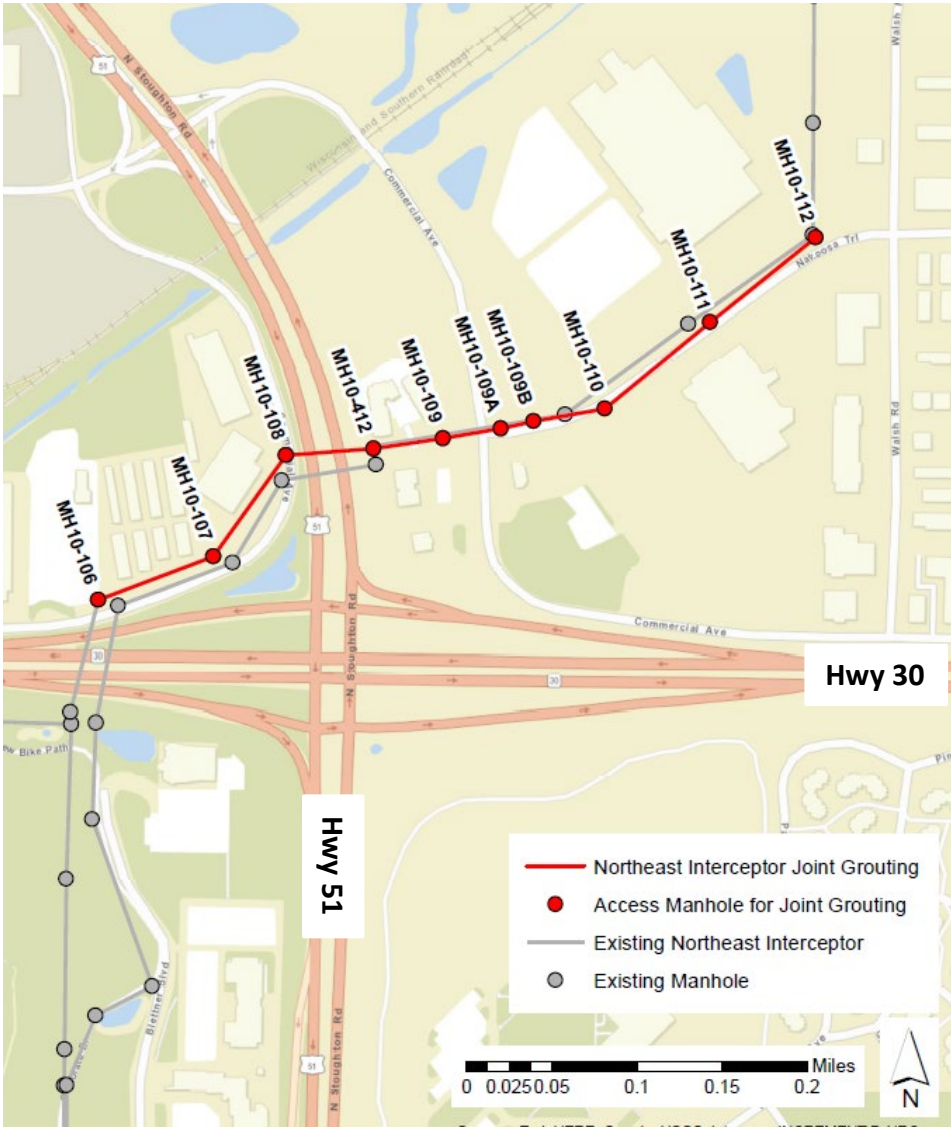

Project Location and Scope

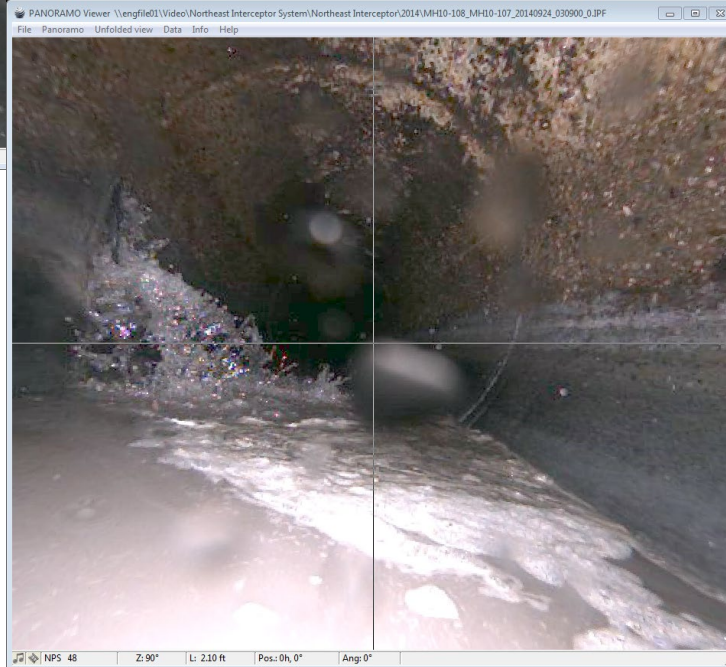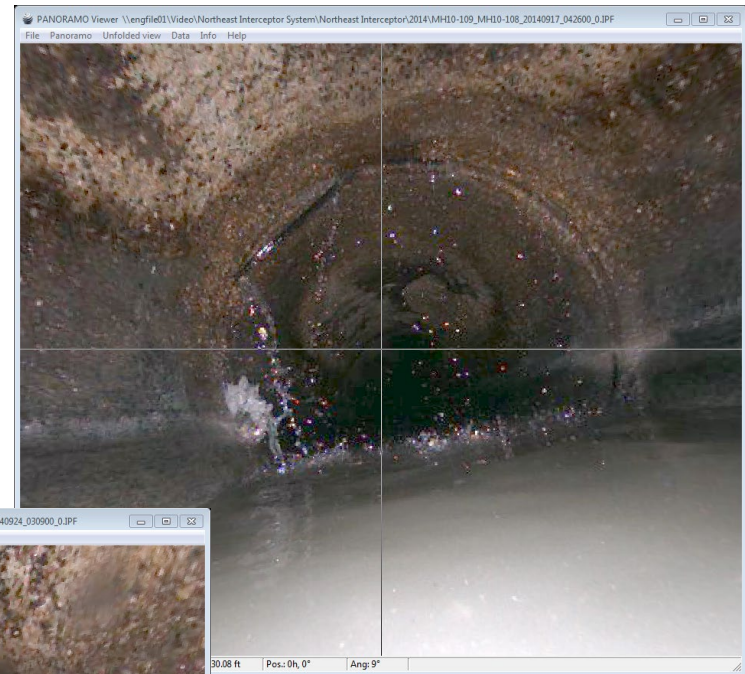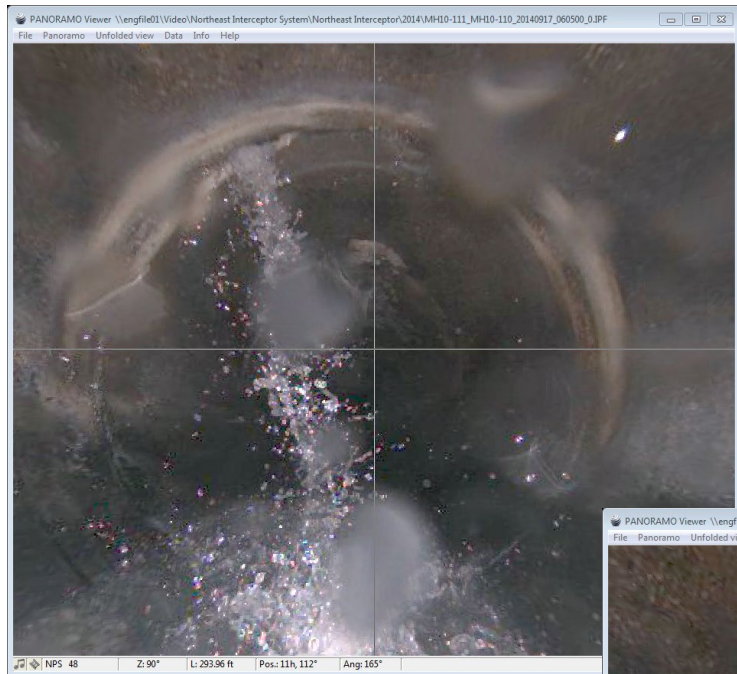

Joint Grouting Technology - Packer

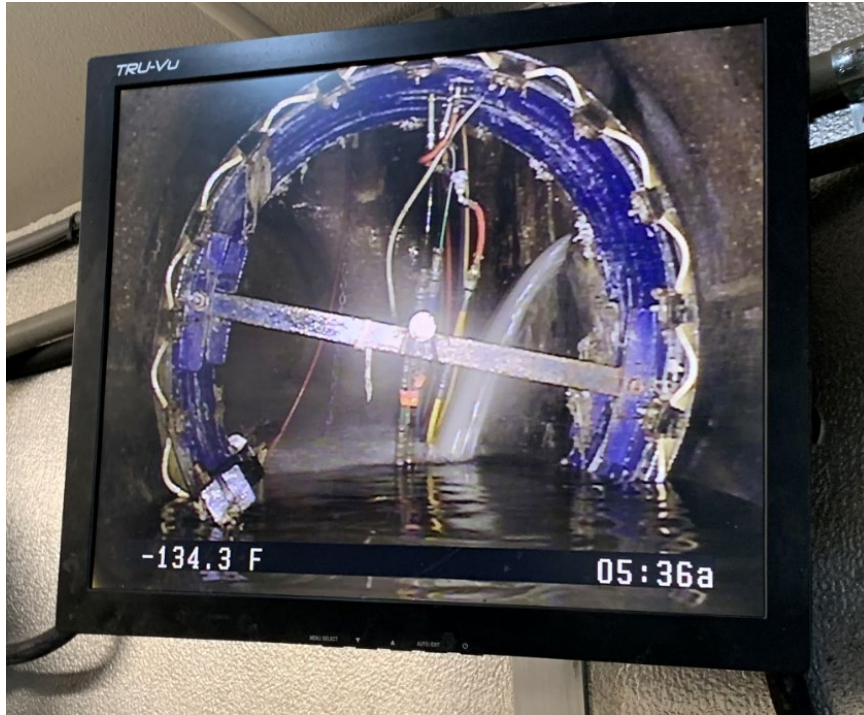

front view



side view

Joint Grouting Technology - Grout



Joint Grouting Technology - Install



Project Video: Before

NAK005A TRL

10-412

12-108



Project Video: During

Upstream MH: MH10-412
Downstream MH: MH10-108
Date: 10/30/2020



Project Video: After

Upstream MH: MH10-412
Downstream MH: MH10-108
Date: 10/30/2020



Contractor Financials

- **Bid Amount:**
\$208,186
- **3 Change Orders**
issued in
construction
- **Final Amount:**
\$191,225 (-8%)


Madison Metropolitan Sewerage District



Overall Financials

- **Total Approved Budget:**
\$304,000
- **Total Project Cost:**
\$201,509 (-33%)

Madison Metropolitan Sewerage District

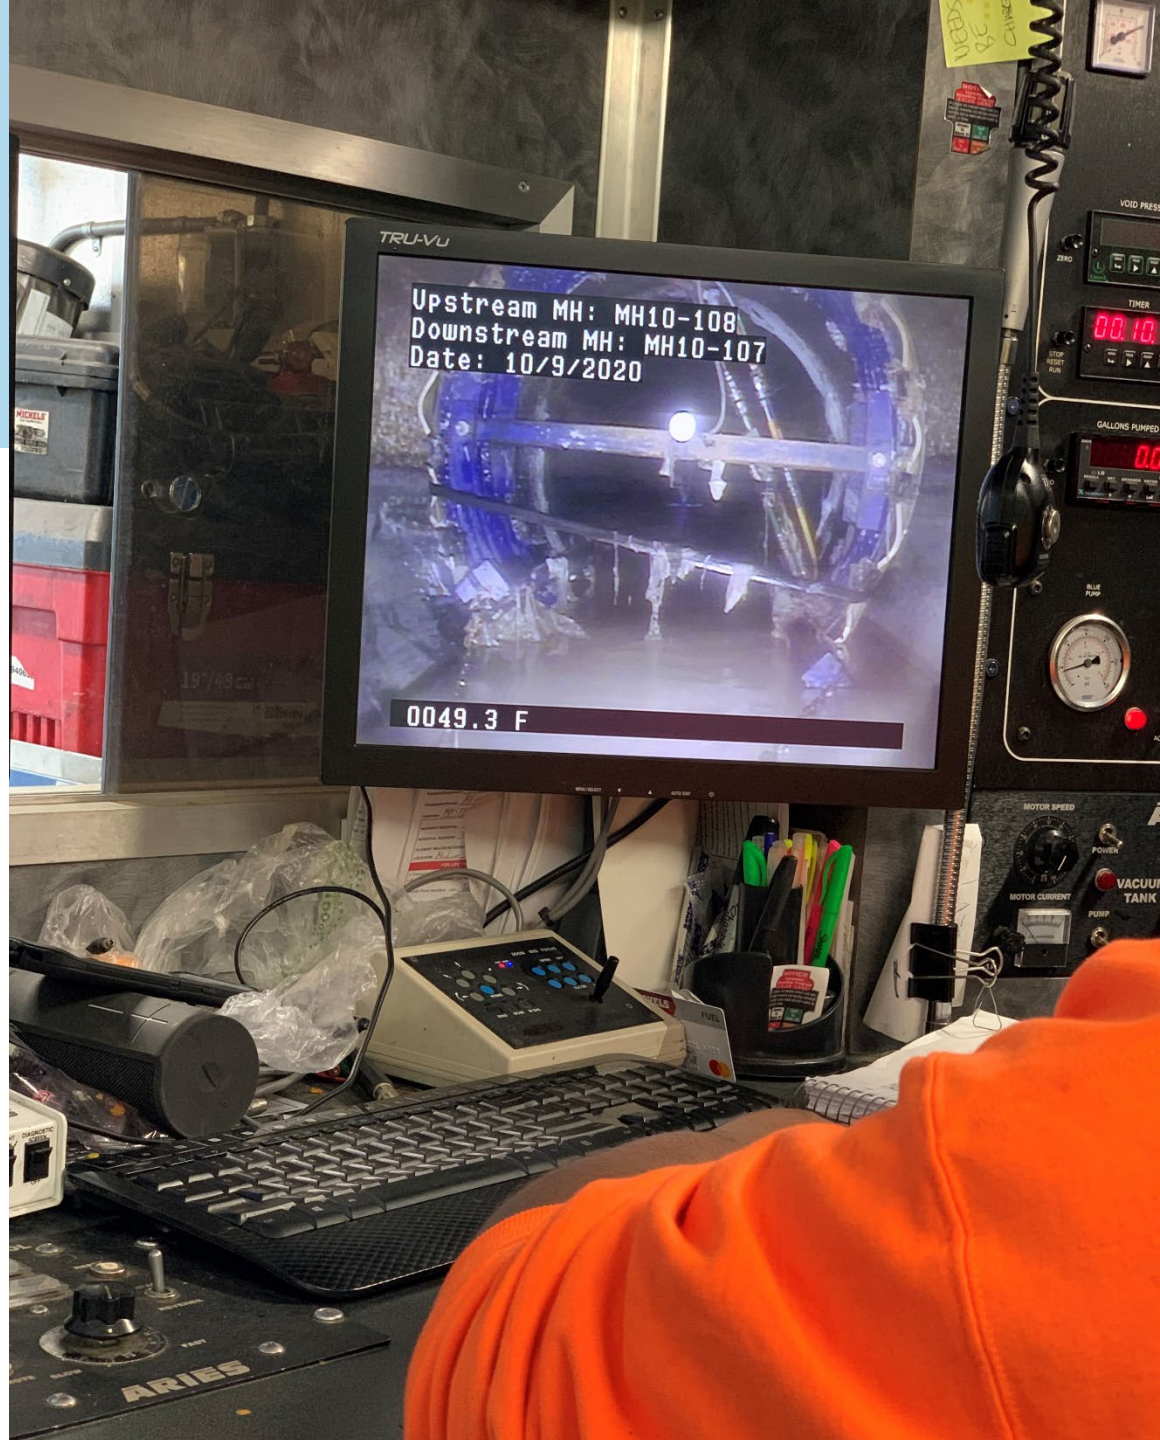

Schedule

- Contract extended ~6 months to allow completion.
- Substantial Completion March, 2021.



Recommendation For 2021-06-10-R11

- Accept the NEI Joint Grouting work per resolution
- \$10,000 maintenance retainer
- If approved, work will be accepted and final payment will be made to Michels Corporation





Thank you!

Madison Metropolitan Sewerage District

